


ID	Task Name	Duration	Start	Finish	Predecessors
1	LIO Interim Space Schedule	153 days	Mon 9/2/13	Wed 4/2/14	
2	Design	108 days	Mon 9/2/13	Wed 1/29/14	
3	Immediately available space programming - 733 W 4th	3 days	Mon 9/2/13	Wed 9/4/13	
4	Immediately available space programming 425 G Street 7th floor	3 days	Mon 9/2/13	Wed 9/4/13	
5	Meeting with LIO Staff to refine program	2 days	Thu 9/5/13	Fri 9/6/13 4	
6	Refine Draft layout of LIO Space	3 days	Mon 9/9/13	Wed 9/11/13 5	
7	Draft Layout of legislature office space	3 days	Mon 9/9/13	Wed 9/11/13 5	
8	Meeting with LIO Staff to Approve plan	0 days	Wed 9/11/13	Wed 9/11/13 7,6	
9	Permit Drawings - 733 W. 4th	15 days	Thu 9/12/13	Wed 10/2/13 8	
10	Permit Drawings 425 G Street	15 days	Thu 9/12/13	Wed 10/2/13 8	
11	Locate Other available spaces for legislative offices	40 days	Thu 10/3/13	Wed 11/27/13 10	
12	Draft Layout - other available spaces	10 days	Thu 11/28/13	Wed 12/11/13 11	
13	Review Layout with Committee	5 days	Thu 12/12/13	Wed 12/18/13 12	
14	Permit Drawings - other available spaces	30 days	Thu 12/19/13	Wed 1/29/14 13	
15	Permits	90 days	Thu 10/3/13	Wed 2/5/14	
16	TI Permit - 733 W. 4th	2 days	Thu 10/3/13	Fri 10/4/13 9	
17	TI Permit 425 G Street	2 days	Thu 10/3/13	Fri 10/4/13 10	
18	TI Permit - Other Available Spaces	5 days	Thu 1/30/14	Wed 2/5/14 14	
19	Construction	128 days	Mon 10/7/13	Wed 4/2/14	
20	LIO Temp Space Construction - 733 W 4th	25 days	Mon 10/7/13	Fri 11/8/13 16	
21	Temp Space 425 G Street Construction	25 days	Mon 10/7/13	Fri 11/8/13 17	
22	IT Systems Set-up and Testing 733 W 4th and 425 G Street 7th floor	9 days	Mon 11/4/13	Thu 11/14/13 20SS+20 days	
23	IT Systems relocation from Current Facility	10 days	Mon 11/4/13	Fri 11/15/13 20SS+20 days	
24	Construction Legislature office space other location	30 days	Thu 2/6/14	Wed 3/19/14 18	
25	IT Systems set-up and testing - other location	10 days	Thu 3/20/14	Wed 4/2/14 24	
26	Moving	99 days	Thu 11/14/13	Wed 4/2/14	
27	Move LIO in to Interim Space	2 days	Fri 11/15/13	Mon 11/18/13 22	
28	Complete Vacation of existing LIO building	7 days	Fri 11/15/13	Mon 11/25/13 22	
29	Some Legislative Offices Available in 733 W. 4th	0 days	Thu 11/14/13	Thu 11/14/13 22	
30	Remainder of Legislature offices available	0 days	Wed 4/2/14	Wed 4/2/14 25	

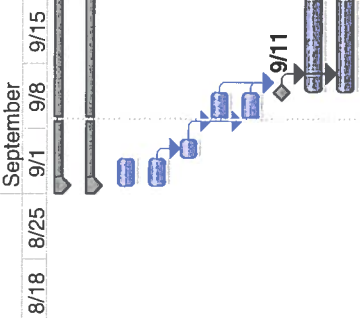

Project: LIO Temp Space Schedule-9.
Date: Mon 9/9/13

Task: Milestone: External Tasks:

Split: Summary: External Milestone:

Progress: Project Summary: Deadline:
